

**BAKERSFIELD CITY SCHOOL DISTRICT
(4) 24X40 TEMPORARY PORTABLE CLASSROOMS
AT WILLIAM PENN ELEMENTARY SCHOOL
BAKERSFIELD, KERN COUNTY, CALIFORNIA**

BID OPENING:
October 2, 2025 at 2:00pm,

Job No. 1318.1
Appl. No. 15-6
File No. 03-123199

ADDENDUM NO. #06

NOTICE TO CONTRACTORS FIGURING THIS WORK

You are hereby notified of the following changes in the plans and specifications, which shall take precedence over anything to the contrary therein.

- 6-1) Refer to DSA Approved Specifications, INDEX and Addendum #05 item 5-1)c. ;
a. DELETE: Typical Classroom Layout in its entirety.
b. ADD: Typical Classroom Layout as attached to this Addendum.
- 6-2) Refer to DSA Approved Drawing No. E2.00 FIRE ALARM SITE PLAN, SYMBOL LEGEND, DETAILS, NOTES & SCHEDULES, FIRE ALARM SYMBOL SCHEDULE and Addendum #04 Item 4-1 c) and 4-2). ;
a. CLARIFY: Existing FACP Hochiki #FIRENET shall be demolished and replaced with Hochiki #LATITUDE.
- 6-3) Refer to DSA Approved Project Manual, INDEX, DIVISION 00 PROCUREMENT & CONTRATING REQUIREMENTS and Addendum #01, Item 1-1)a. , DIVISION 00, Instructions for Procurement, Work Scope BP-01 Electrical, Fire Alarm and Communications;
a. ADD: Work Scope Note 29 as follows;
29. Exclusions
i. Demo of (E) Basketball and tetherball balls. This work is to be performed by the District.
ii. Demo of (E) Tree, root ball, concrete curb and existing fencing. This work is to be performed by the District.
iii. AC Paving at ramps of portable classrooms. This work is to be performed by the District.
iv. Chain link fencing and gates. This work is to be performed by the District.

CONFORMANCE WITH SPECIFICATIONS


All work shall be in conformance with the specifications as they apply to work of a similar nature.




SCARCHITECT, INC.

1601 New Stine Road, Ste. 280
Bakersfield, CA 93309

Stephen J. Corbin, AIA, NCARB, LEED-AP BD+C
Architect

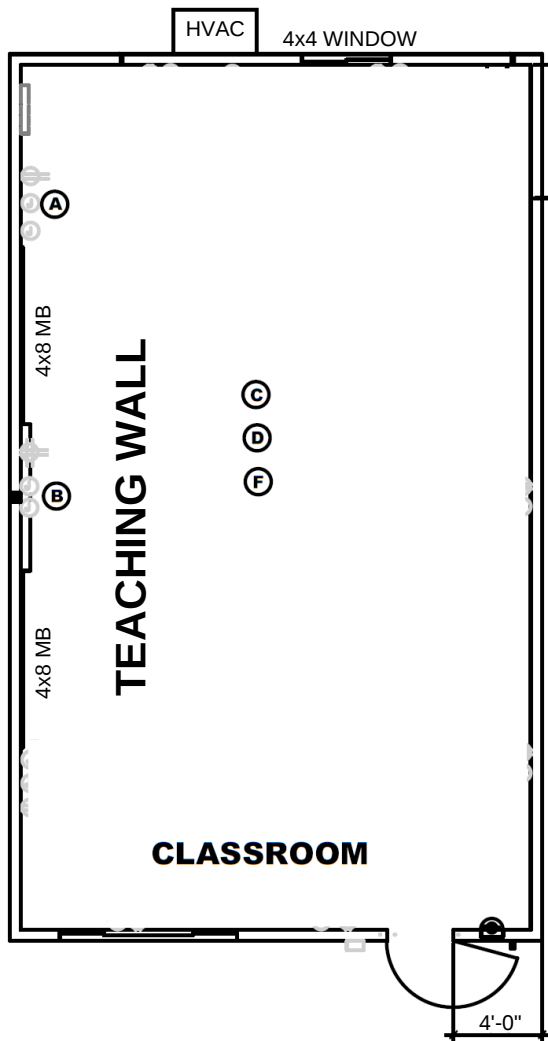

STD BCSD 24x40 CR BLDG
7-7-22

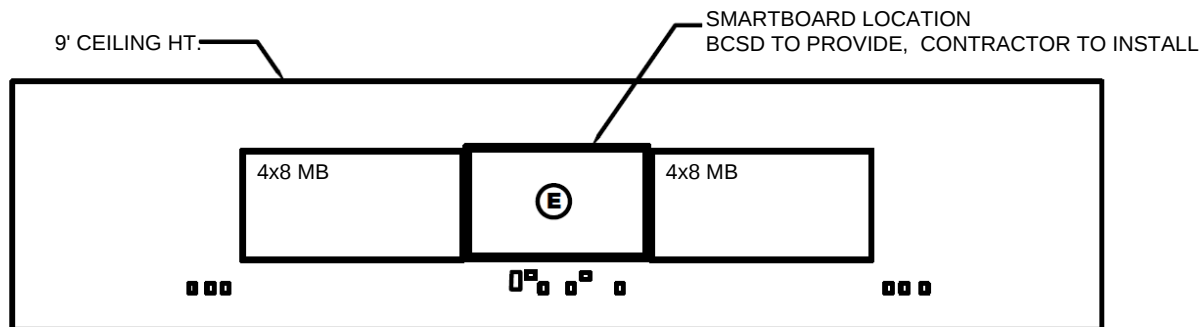

STD 24x40 TEACHING WALL

7-7-22

KEYNOTES

- (A) INSTALL/TERMINATE 3 CAT6 DATA CABLES INTO 3 PORT FACEPLATE
- (B) INSTALL/TERMINATE 2 CAT6 DATA CABLES INTO 3 PORT FACEPLATE
USE BLANK ON 3RD PORT
- (C) INSTALL/TERMINATE 2 CAT6 DATA CABLES ABOVE CEILING TILE
LEAVE COIL BOTH CABLES UP AND ATTACH TO J-HOOK
30FT SPARE LENGTH
- (D) INSTALL/TERMINATE 2 CAT6A DATA CABLES INTO 2 PORT FACEPLATE
ATTACH FACEPLATE TO A 1G LOW VOLTAGE BRACKET INSTALLED IN CEILING TILE
- (E) DISTRICT PROVIDED SMARTBOARD AND ASSOCIATED EQUIPMENT TO BE INSTALLED
ACCORDING TO BCSD SMARTBOARD/LCD INSTALLATION METHODS AND REQUIREMENTS
- (F) INSTALL CEILING MOUNTED CLASSROOM SPEAKER
SPEAKER TO BE CONNECTED/PROGRAMMED TO DISTRICT P/BELL SYSTEM
VALCOM CLASS CONNECTION

ADDENDUM #06,
 ITEM 6-1)b

BCSD 24x40 CR BLDG

SMARTBOARD/DATA INSTALL NOTES
