

# CLASS LEASING, LLC.

1221 Harley Knox Blvd. Perris, CA 92571-7408  
(951) 943-1908 Fax (951) 943-5768

## SPECIFICATIONS RELOCATABLE CLASSROOMS

- 3.01 CARPENTRY:**  
1. **Scope of Work:** Contractor shall provide all labor, materials and services to install carpentry.  
2. **Workmanship:**  
a) **FRAMING:** securely nailed, bridged and blocked to form rigid structure. Work cut, fitted and assembled level, plumb and true to line. Trim in as long lengths as possible with all standing trim in one piece. Trim sealed at all edges.  
b) **NAILING:** in accordance with the title 24 CCR-Table 2304.9.1. Nails shall be corrosion resistant box nails.  
c) Machine applied nailing shall have prior demonstration and approval by DSA Field Inspector and the Architect. The approval is subject to continuous satisfactory performance. Plywood shall have a minimum thickness of 3/8". If nail heads penetrate the outer ply more than would be normal for a hand hammer or if minimum allowable edge distances are not maintained, the performance will be deemed unsatisfactory.  
d) **TRIM:** sealed at all edges. Sealant painted to match trim or siding.

- 4.01 MATERIAL SPECIFICATIONS:**  
1. Structural framing shall be Hem Fir-Larch graded in accordance with the standard grading rules of the Western Wood Products Association or standard grading rules No. 16 of the West Coast Lumber Inspection Bureau, latest editions. Grades shall be as follows unless noted otherwise on the drawings. (Hem Fir South is not allowed.) Each piece shall be grade marked and no piece may fall below grades indicated. All framing except as noted Hem Fir No. 2  
2. Plywood shall be as shown on these drawings with exterior glue in accordance with U.S. Product Standard PS 1-07. All panels shall be marked with an APA grade mark with an identification index as shown on drawings. Use 4x8 panels minimum, except at boundaries and at framing changes where minimum panel dimension shall be 24" at roofs and floors and 12" at walls.  
3. Bolts for timber connections shall conform to ANSI/ASME Standard B18.2.1-2012 & 2012 edition of NDS (the National Design Specification for Wood Construction by the National Forest Products Association). Bolts shall be installed in accordance with the requirement of 2012 NDS. Bolt holes shall be 1/2 to 1/16 inch larger than bolt diameter. Bolts shall be full body steel bolts with minimum yield strength of 45,000 PSI. Re-tighten bolts before closing work.  
4. Lag screws shall be steel and conform to ANSI/ASME Standard B18.2.1 and 2012 NDS. Holes for lag screw shanks shall be bored the same depth and diameter as the shank. The remaining depth of penetration of the screw shall be bored to 70% of the shank diameter. One quarter inch (1/4") diameter lag screws need not have pre-drilled holes if it can be shown that wood members are not damaged during installation. Provide full diameter body lag screws with bending yield strengths per Table 11J in NDS  
5. Provide malleable iron washers or equivalent cut plate washers (not less than a standard cut washer) under nuts and /bolt or lag screw heads which bear on wood.  
6. Wood screws shall conform to ANSI/ASME Standard B18.6.1 and the requirements of the 2012 NDS. Galvanized or other corrosion resistant coating where exposed to weather or used in foundations. Screws shall be steel with cut threads and bending yield strengths per Table 11L in NDS.  
7. Wood members shall be cut or notched only as shown on structural drawings.  
8. When required nailing tends to split wood members, nail holes shall be pre-bored to 3/4 of the nail diameter.  
9. Structural nailing shall be with BOX NAILS per all requirements of 2012 NDS. Nailing not specifically indicated shall comply with CCR Title 24, Part 2, Table 2304.9.1. All nails shall be galvanized or other corrosion resistant coating where exposed to weather, in foundations and as noted on plans, per the requirements of CCR Title 24, Part 2, with minimum bending yields per table 11N in NDS. (See nail equivalence below.)  
10. Nail equivalents:  
(provide minimum nail lengths as required for specified penetration, TYPICAL: U.N.O.)  
6d equals .113" DIA. - provide 1.36" minimum point penetration  
8d equals .131" DIA. - provide 1.57" minimum point penetration

11. Pressure preservative treatment shall be per Section 2303.1.8, CCR Title 24, Part 2. Provide quality mark on all treated foundation members that comply with CBC 2303.1.8.1. All foundation members shall be marked as "For ground contact" or "For above ground use" as appropriate. Pressure treated material shall comply with AWPA Standard U1 as required by CBC 2303.1.8. Treat all cut ends of pressure treated members with an approved preservative. (Wiltard Wood Copper Green 2% or an approved equivalent). Where noted, members below the sub floor that are not a part of the foundation shall be pressure treated.  
12. Only material in contact with ground needs to be pressure treated, all other foundation lumber can be DF or HF#2 or equal.  
13. If machine nailing is utilized for this project, contractor shall comply with all requirements of CCR Title 24, Part 2. Machine nailing is subject to approval by the Structural Engineer or Architect and the Division of the State Architect.  
14. Fasteners for pressure-preservative treated and fire-retardant treated wood shall comply with Section 2304.9 of CBC.  
15. Nails and spikes used in wet or exterior locations shall comply with Section 2304.9.1.1 of CBC.  
16. Shim material shall be plywood CD EXP 1 or equal (not pressure treated).  
17. Used lumber in good condition is acceptable for use in foundation system.  
18. Tie plates shall conform to A-1011 Grade 33.

- 5.01 SITE INSTALLATION REQUIREMENTS FOR DSA CLASSROOM BUILDINGS:**  
In the case of equipment located in the State of California, the LESSEE (School District) is responsible for the site being cleared (free of grass, trees, shrubs, etc) and graded to within 4 1/2" of level grade for each building. If the site exceeds the 4 1/2" level grade requirement additional costs may be charged to lessee.  
Under no circumstances should the site be greater than 9" from level grade or have less than a 1000 PSF MINIMUM SOIL BEARING PRESSURE.  
Prior to delivery, the lessee shall mark the four corners of the building on the site, including door location. Should special handling be required to either place, install or relocate the classroom on the lessee's site due to site obstruction such as fencing, landscaping, other classrooms, etc., additional costs will be charge to the lessee.

- 6.01 TEST AND INSTALLATION:**  
1. Provide Electrical Grounding Test per DSA IR E-1.  
2. Field Welding for welded tie plate option. (If used, requires Test and Inspection.)  
The example form DSA 103's shown on this sheet are for illustration purposes only. A form DSA 103 is to be completed for each application that this PC is being incorporated into and all example form DSA-103's are to be crossed out on this drawing.  
3. No other tests and inspections are required.

- 1.01 GENERAL REQUIREMENTS:**  
1. The requirements of the general conditions of the agreement and these General Requirements apply to the several trade sections with the same force as though fully repeated in each section.  
2. Name brands are indicated to establish a standard of quality. Items of equal or better quality may be substituted for the listed brand named products.

- 1.02 SCOPE OF WORK:**  
1. The work consists of installing on-site, modular Relocatable buildings as defined herein, shown and detailed on the drawings.  
2. All requirements of CCR (California Code of Regulation) Title 19 and 24 relating to inspections and verified reports shall be completed with and shall include:  
a) General responsible charge of Field Administration by the Architect of Record.  
b) Inspection during the course of construction by an Inspector approved by DSA (Division of the State Architect) and the District Architect. The Inspector shall be responsible for and approved to inspect the general construction, welding, mechanical and electrical work. Cost of these inspections shall be borne by the School District.  
c) On site inspection of the building installation, electrical and utility of the building installation or connection by an Inspector approved by the DSA and retained by the School District.  
d) Other special tests or inspections as may be required by DSA. Cost of these inspections/tests shall be borne by the School District.

- 1.03 WORK NOT INCLUDED:**  
1. All on-site or off-site utilities and the connection of them to the building unless indicated on the drawings.  
2. All leveling, grading or other site preparation (except concrete or wood leveling strips, where Required) unless otherwise indicated on the drawings.  
3. Fire alarm system, program bell, clock, public address system, intercom system, TV system, computer data or any other low voltage system, unless otherwise indicated on the drawings or the lease agreement.

- 1.04 ACCESSIBILITY OF SITE:**  
The School District shall provide access to the site for the installation of the building. Removal of trees, shrubs, fencing, sprinklers, etc. necessary for move-in and removal of the buildings shall be the responsibility of the School District and the District Architect.

- 2.01 SITE ASSEMBLY:**  
1. **Scope of Work:** Contractor shall provide all labor, materials and services to prepare the building elements, transport them from the plant to the site and to complete the assembly at the site.  
The condition of the site, such as drainage and soil bearing capacity, shall be the responsibility of the School District and the District Architect.  
2. **Assembly of Elements:**  
a) In a location on the site as determined by the District Architect. The contractor shall place the foundation as detailed on the drawings.  
b) The elements shall be brought to the site on wheel assembly and transferred to the prepared site. Great care shall be taken to avoid damage to the elements by racking or bumping.  
c) Connection of the elements together shall be done according to instructions on the drawings. Flashing, trim and other loose items shall be installed per plans and details of the original building manufacturer's drawings.

**DSA** STATE OF CALIFORNIA  
**Statement of Structural Tests & Special Inspections - 2013 CBC**

Project Name: \_\_\_\_\_ DSA File No.: \_\_\_\_\_  
Application No.: \_\_\_\_\_  
Date Submitted: \_\_\_\_\_  
Inspector: \_\_\_\_\_  
Contractor: \_\_\_\_\_

**17. STRUCTURAL STEEL AND COLD-FORMED STEEL USED FOR STRUCTURAL PURPOSES**  
a. Verify steel materials are properly marked and that all certificates indicate material properties that comply with applicable requirements.  
b. Verify steel materials are properly marked and that all certificates indicate material properties that comply with applicable requirements.  
c. Verify steel materials are properly marked and that all certificates indicate material properties that comply with applicable requirements.

TEST OR SPECIAL INSPECTION	CODE REFERENCE AND NOTES
BOILS	
CONCRETE	Table 1706.3
MASONRY	Table 1706.3 and 1706.4
STEEL	Table 1706.3
17. STRUCTURAL STEEL AND COLD-FORMED STEEL USED FOR STRUCTURAL PURPOSES	
18. WELDING	Table 1706.3 and 1706.4
19. FIELD WELDING	Table 1706.3
WOOD	
OTHER	

1. Field Working Inspector: Special Inspection Verified Report - Form DSA-202

KEY TO COLUMN	1. Type	2. Performed by
Continuance	Indicates that a continuous special inspection is required	Indicates that the special inspection is to be performed by a registered professional engineer or his or her designee
Periodic	Indicates that a periodic special inspection is required	Indicates that the test or inspection is to be performed by a testing laboratory approved by the DSA Laboratory Evaluation and Acceptance (LEA) Program. See section 4.0.5, ESR-32, Title 24, Part 2.
Test	Indicates that a test is required	Indicates that the special inspection is to be performed by the project inspector
SI	Indicates that the special inspection is to be performed by a special inspector	Indicates that the special inspection is to be performed by a special inspector

**APPLICABLE BUILDING CODES**  
ALL NEW WORK SHALL COMPLY AND CONFORM TO THE REQUIREMENTS OF THE 2013 CBC  
**2013 CALIFORNIA CODE OF REGULATIONS (CCR) As of January 01, 2014\***  
(2013 CALIFORNIA BUILDING STANDARDS ADMINISTRATIVE CODE PART 1, TITLE 2  
(2012 INTERNATIONAL BUILDING CODE VOLUMES 1-2 WITH 2013 CALIFORNIA AMENDMENTS)  
-2013 CALIFORNIA ELECTRICAL CODE (CEC) PART 3, TITLE 24, CCR  
(2011 NATIONAL ELECTRICAL CODE WITH 2013 CALIFORNIA AMENDMENTS)  
-2013 CALIFORNIA MECHANICAL CODE (CMC) PART 4, TITLE 24, CCR  
(2012 INTERNATIONAL MECHANICAL CODE WITH 2013 CALIFORNIA AMENDMENTS)  
-2013 CALIFORNIA PLUMBING CODE (CPC) PART 5, TITLE 24, CCR  
(2012 UNIFORM PLUMBING CODE WITH 2013 CALIFORNIA AMENDMENTS)  
-2013 CALIFORNIA FIRE CODE (CEC) PART 6, TITLE 24, CCR\*  
-2013 CALIFORNIA ENERGY CODE PART 9, TITLE 24, CCR  
(2012 INTERNATIONAL FIRE CODE WITH 2013 CALIFORNIA AMENDMENTS)  
-2013 CALIFORNIA REFERENCED STANDARDS CODE PART 12, TITLE 24, CCR  
TITLE 19 CCR PUBLIC SAFETY, STATE FIRE MARSHALL REGULATIONS.

**DESIGN DATA:**  
FLOOR LIVE LOAD = 50 PSF, 50 + 20 PSF PARTITIONS, 100 PSF  
ROOF LIVE LOAD = 20 PSF REDUCIBLE FOR TRIBUTARY AREA  
WIND SPEED = 120 MPH (V) (3 SECOND GUST), Kz = 1.0  
SNOW LOAD: PROJECT IS NOT LOCATED IN A SNOW REGION  
BUILDING CODES = 2012 IBC AND CBC 2013


**SEISMIC DESIGN DATA:**  
Basic Seismic-Force-Resisting System = STEEL MOMENT FRAME  
ANALYSIS PROCEDURE USED = EQUIVALENT LATERAL FORCE  
Seismic Design Category = E (per CBC Section 1613A.6.2)  
Design Base Shear: 24x40 BUILDING = 8400 # (Roof, Floor, Walls & Partitions)  
36x40 BUILDING = 14160 # (Roof, Floor, Walls & Partitions)  
48x40 BUILDING = 18240 # (Roof, Floor, Walls & Partitions)

**SEISMIC DESIGN DATA:**  
Basic Seismic-Force-Resisting System = WOOD PANEL SHEAR WALLS  
ANALYSIS PROCEDURE USED = EQUIVALENT LATERAL FORCE  
Seismic Design Category = E (per CBC Section 1613A.6.2)  
Design Base Shear: 24x40 BUILDING = 8400 # (Roof, Floor, Walls & Partitions)  
36x40 BUILDING = 14160 # (Roof, Floor, Walls & Partitions)  
48x40 BUILDING = 18240 # (Roof, Floor, Walls & Partitions)

**SEISMIC DESIGN DATA:**  
Basic Seismic-Force-Resisting System = WOOD PANEL SHEAR WALLS  
ANALYSIS PROCEDURE USED = EQUIVALENT LATERAL FORCE  
Seismic Design Category = E (per CBC Section 1613A.6.2)  
Design Base Shear: 24x40 BUILDING = 8400 # (Roof, Floor, Walls & Partitions)  
36x40 BUILDING = 14160 # (Roof, Floor, Walls & Partitions)  
48x40 BUILDING = 18240 # (Roof, Floor, Walls & Partitions)

**LIMITATIONS FOUNDATION PC ONLY:**  
FOUNDATION ONLY PC IS DESIGNED TO SUPPORT THE SUPERSTRUCTURE FOR THE RELOCATABLE BUILDINGS AS LISTED ON THIS DRAWING.  
THE DESIGN CALCULATIONS ARE BASED ON THE FOLLOWING:  
1. DSA APPROVED STOCKPILE BUILDINGS  
2. ROOF OVERHANGS OF 5'-0" MAXIMUM  
3. SINGLE SLOPE OR DUAL SLOPE BUILDINGS  
WALL HEIGHT: 9'-0" MAXIMUM ON DUAL SLOPE BUILDING  
WALL HEIGHT: 10'-4" MAXIMUM ON SINGLE SLOPE BUILDING  
(HEIGHT DETERMINED FROM FINISH FLOOR IN BUILDING TO BOTTOM OF STEEL ROOF STRUCTURE; BEAMS OR ROOF HEADERS)  
WALL HEIGHT: 9'-0" MAXIMUM ON SHEAR WALL-DUAL SLOPE BUILDING  
4. WALL DEAD LOAD OF 10 PSF (NO STUCCO)  
5. FLOOR DEAD LOAD OF 8 PSF

**DESIGN DATA:**  
FLOOR LIVE LOAD = 50 PSF, 50 + 20 PSF PARTITIONS, 100 PSF  
ROOF LIVE LOAD = 20 PSF REDUCIBLE FOR TRIBUTARY AREA  
WIND SPEED = 120 MPH (V) (3 SECOND GUST), Kz = 1.0  
SNOW LOAD: PROJECT IS NOT LOCATED IN A SNOW REGION  
BUILDING CODES = 2012 IBC AND CBC 2013

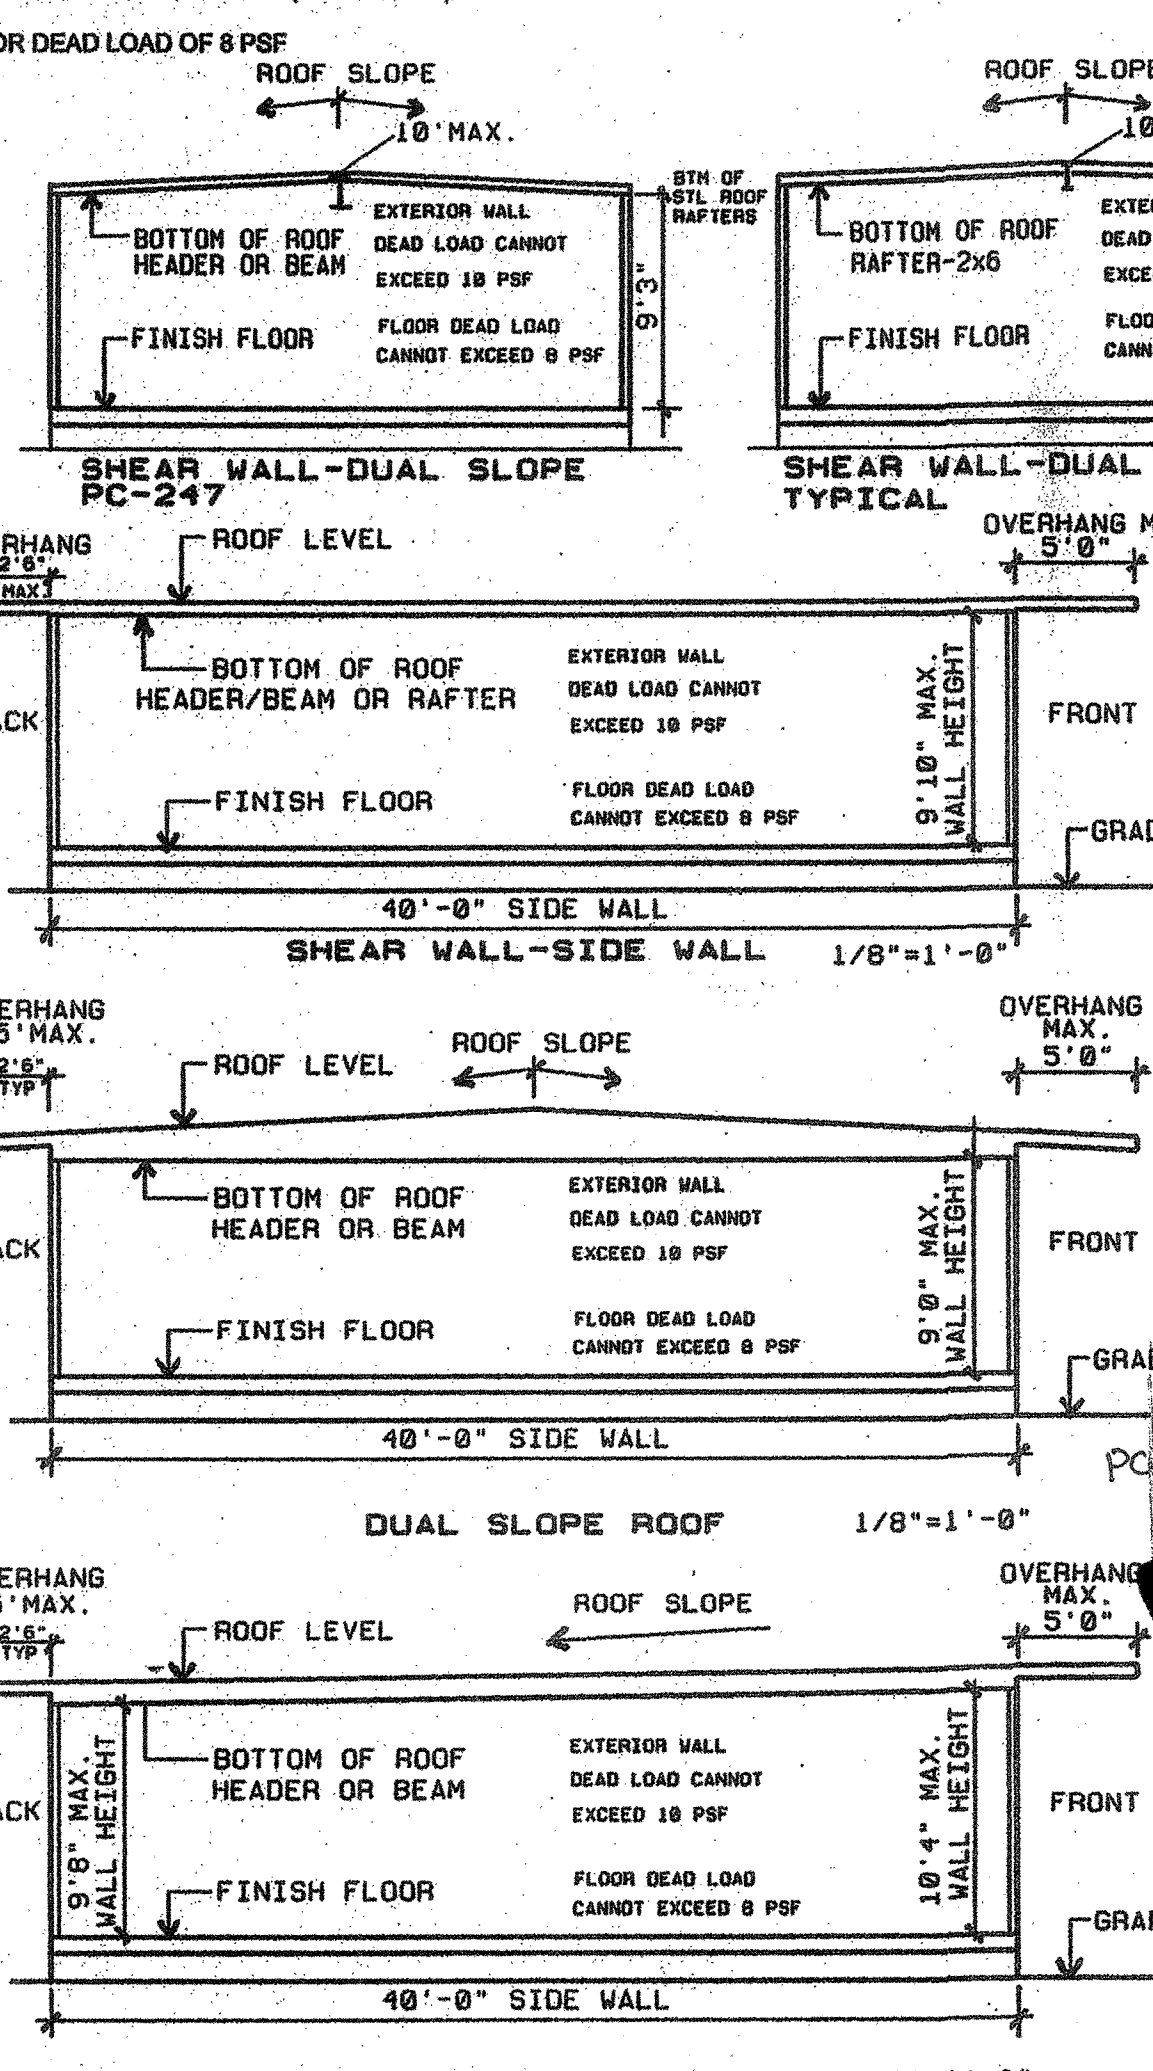

TYPICAL ELEVATIONS ARE SHOWN TO CLARIFY FOUNDATION PC ONLY LIMITATIONS  
DOCUMENTATION SHALL BE PROVIDED BY ENGINEER OF GENERAL RESPONSIBLE CHARGE  
TO BE REVIEWED AND APPROVED BY THE DSA STRUCTURAL PLAN REVIEWER.

**SCOPE OF WORK:** DSA FOUNDATION PLANS FOR EXISTING STOCKPILE BUILDINGS FOR CLASS LEASING, LLC.  
**SHEET INDEX: STOCKPILE BUILDING FOUNDATION - 2013 CODE UPDATE**  
F1.0 COVER SHEET, BUILDING DATA, STOCKPILE APPROVAL INDEX  
F2.0 24x40 50 PSF FOUNDATION PLAN AND DETAILS, ADJACENT BUILDING PAD  
F2.1 24x40 50+20 PSF FOUNDATION PLAN AND DETAILS, ADJACENT BUILDING PAD  
F2.2 24x40 50 PSF FOUNDATION PLAN AND DETAILS, ADJACENT BUILDING PAD  
F2.3 36x40 50+20 PSF FOUNDATION PLAN AND DETAILS, ADJACENT BUILDING PAD  
F2.4 36x40 50 PSF FOUNDATION PLAN AND DETAILS, ADJACENT BUILDING PAD  
F4.0 48x40 50 PSF FOUNDATION PLAN AND DETAILS, ADJACENT BUILDING PAD  
F4.1 48x40 50+20 PSF FOUNDATION PLAN AND DETAILS, ADJACENT BUILDING PAD  
F4.2 48x40 100 PSF FOUNDATION PLAN AND DETAILS, ADJACENT BUILDING PAD

**SHEET INDEX:**  
**BELOW GRADE CONCRETE FOUNDATION - DESIGNED FOR MODTECH BUILDINGS ONLY**  
C1.0 COVER SHEET, BUILDING DATA, STOCKPILE APPROVAL INDEX  
C2.0 24 x 40 - 50 PSF CONCRETE FOUNDATION PLAN & DETAILS, ADJACENT BUILDING PAD  
C2.1 24 x 40 - 50+20 PSF CONCRETE FOUNDATION PLAN & DETAILS, ADJACENT BUILDING PAD  
C3.0 36 x 40 - 50 PSF CONCRETE FOUNDATION PLAN & DETAILS, ADJACENT BUILDING PAD  
C3.1 36 x 40 - 50+20 PSF CONCRETE FOUNDATION PLAN & DETAILS, ADJACENT BUILDING PAD  
C3.2 36 x 40 - 50 PSF CONCRETE FOUNDATION PLAN & DETAILS, ADJACENT BUILDING PAD  
C4.0 48 x 40 - 50 PSF CONCRETE FOUNDATION PLAN & DETAILS, ADJACENT BUILDING PAD  
C4.1 48 x 40 - 50+20 PSF CONCRETE FOUNDATION PLAN & DETAILS, ADJACENT BUILDING PAD  
C4.2 48 x 40 - 100 PSF CONCRETE FOUNDATION PLAN & DETAILS, ADJACENT BUILDING PAD

**ADJACENT BUILDINGS:** ONLY THOSE BUILDINGS MANUFACTURED BY THE SAME COMPANY MAY BE PLACED ADJACENT TO EACH OTHER

**CLASS LEASING APPROVED STOCKPILE A NUMBERS FOR THIS FOUNDATION PC**

BUILDING DATA - 24 X 40 SHEAR WALL						
STPK #	DSA #	PC-BASE	DATE	SIZE	FLOOR LOAD	BLDG MFG
STPK 029	62943	SHR	10-21-1998	24 x 40	50+20#	MODTECH
STPK 02	62912	48138-SHR	11-06-1999	24 x 40	50#	MODTECH
STPK 01	62913	46760-SHR	11-06-1999	24 x 40	50#	MODTECH
STPK 03	62914	4SHR	11-06-1999	24 x 40	50#	MODTECH
STPK 06	62918	45400-SHR	12-07-1999	24 x 40	50#	MODTECH
STPK 04	62919	SHP PC 29 SHR	12-07-1999	24 x 40	50#	MODTECH
STPK 22	65113	PC 96	05-14-1994	24 x 40	50#	MODTECH
STPK 24	65880	PC 96	05-14-1994	24 x 40	50#	MODTECH
STPK 13	61997	PC 247	06-29-1994	24 x 40	50#	MODTECH
STPK 77	67970	PC 247	11-10-1997	24 x 40	50#	MODTECH

BUILDING DATA - 24 X 40 RIGID FRAME						
STPK #	DSA #	PC-BASE	DATE	SIZE	FLOOR LOAD	BLDG MFG
STPK 11	52482	MRF	06-13-1991	24 x 40	50+20#	MODTECH
STPK 20	55031	PC 79	09-18-1990	24 x 40	50#	MODTECH
STPK 21	55032	PC 79	09-18-1990	24 x 40	50#	MODTECH
STPK 23	55247	PC 79	11-26-1990	24 x 40	50#	MODTECH
STPK 9W	57194	PC 79	11-08-1991	24 x 40	50+20#	MODTECH
STPK 14	57679	PC 96	03-19-1992	24 x 40	50#	MODTECH
STPK 16	53298	PC 243	05-04-1995	24 x 40	50#	MODTECH
STPK 18	53321	PC 242	05-11-1995	24 x 40	50#	MODTECH
STPK 27	55493	PC 266	07-31-1996	24 x 40	50#	MODTECH
STPK 31	66318	PC 266	11-12-1996	24 x 40	50+20#	MODTECH
STPK 33	67333	PC 266	03-11-1997	24 x 40	50#	MODTECH
STPK 35	04-100117	PC 266	01-15-1999	24 x 40	50+20#	MODTECH
STPK 39	04-100128	PC 275	05-10-1998	24 x 40	50+20#	MODTECH
STPK 37	04-100598	PC 266	08-10-1998	24 x 40	50+20#	MODTECH
STPK 40	04-100690	PC 262	09-03-1998	24 x 40	50+20#	MODTECH
STPK 42	04-100929	PC 266	01-07-1999	24 x 40	50+20#	MODTECH
STPK 43	04-101555	PC 275	05-09-1999	24 x 40	50#	MODTECH
STPK 44	04-101902	PC 266	05-26-1999	24 x 40	50+20#	MODTECH
STPK 48	04-101763	PC 101268	12-18-1999	24 x 40	50#	MODTECH
STPK 81	04-102016	PC 101268	03-16-2000	24 x 40	50# / 50+20#	MODTECH
STPK 63	04-102365	PC 101268	07-06-2000	24 x 40	50+20#	MODTECH
STPK 66	04-102824	PC 101268	12-21-2000	24 x 40	50#	MODTECH
STPK 62	04-104169	PC 101268	04-18-2002	24 x 40	50+20#	MODTECH
STPK 67	04-104912	PC 101268	12-05-2002	24 x 40	50+20#	MODTECH
STPK 70	04-106290	PC 104891	05-22-2003	24 x 40	50+20#	MODTECH
STPK 75	04-110431	PC 04-105337	06-05-2003	24 x 40	50#	MODTECH
STPK 76	04-105455	PC 04-104798	07-17-2003	24 x 40	50#	MODTECH
STPK 78	04-109208	PC 106884	12-03-2007	24 x 40	50#	CURRENT/MSI
STPK 107	65995	PC 266	05-24-1996	24 x 40	50#	MODTECH
STPK 109	63341	PC 275	05-20-1999	24 x 40	50#	MODTECH
STPK 110	04-100118	PC 04-100073	01-18-1998	24 x 40	50#	MSI
STPK 111	04-101984	PC 04-101419	03-09-2000	24 x 40	50#	MODTECH
STPK 112	04-104082	PC 04-101419	03-21-2002	24 x 40	50#	MODTECH
STPK 113	04-104310	PC 04-101419	06-02-2002	24 x 40	50#	MODTECH
STPK 114	04-105455	PC 04-104798	07-17-2003	24 x 40	50#	MODTECH
STPK 130	04-101927	PC 270	03-12-1999	24 x 40	50# / 50+20#	MODTECH
STPK 151	04-104946	PC 04-101419	01-23-2003	24 x 40	50# / 50+20#	MODTECH

BUILDING DATA - 36 X 40 RIGID FRAME						
STPK #	DSA #	PC-BASE	DATE	SIZE	FLOOR LOAD	BLDG MFG
STPK 3W	57194	PC 79	11-08-1991	36 x 40	70#	MODTECH
STPK 32	66319	PC 266	11-12-1998	36 x 40	50+20#	MODTECH
STPK 34	67332	PC 266	03-11-1997	36 x 40	50+20#	MODTECH
STPK 45	04-101618	PC 101268	10-07-1999	36 x 40	50+20#	MODTECH
STPK 61	04-113121	PC 04-102016	09-12-2013	36 x 40	50+20#	MODTECH
STPK 67	04-103901	PC 101268	09-01-2001	36 x 40	50#	MODTECH
STPK 69	04-104447	PC 101268	07-11-2002	36 x 40	50+20#	MODTECH
STPK 71	04-106-410	PC 104891	07-26-2004	36 x 40	50+20#	MODTECH
STPK 73	04-106885	PC 101268	03-01-2007	36 x 40	100#	MODTECH
STPK 86	04-111010	PC 79	06-03-2010	36 x 40	50+20#	MODTECH
STPK 104	04-113588	A-58118	05-01-2014	36 x 40	50+20#	MODTECH

BUILDING DATA - 48 X 40 RIGID FRAME						
STPK #	DSA #	PC-BASE	DATE	SIZE	FLOOR LOAD	BLDG MFG
STPK 9W	57194	PC 79	11-08-1991	48 x 40	100#	MODTECH
STPK 3W	57194	PC 79	11-08-1991	48 x 40	70#	MODTECH
STPK 17	63289	PC 243	05-04-1995	48 x 40	50+20#	MODTECH
STPK 41	04-100797	PC 269	10-22-1998	48 x 40	50+20#	MODTECH
STPK 46	04-101917	PC 101268	10-07-1999	48 x 40	50+20#	MODTECH
STPK 63	0					
