

ROOM FINISH SCHEDULE

ROOM NO.	DESCRIPTION	FLOOR	BASE	WALLS				CEILING		REMARKS	ROOM NO.
				NORTH	EAST	SOUTH	WEST	MATL	HEIGHT		
101	LOBBY	10A	6A	-	2A	-	-	IA	4'-0"	-	101
102A	CLERK	2A	1A	2A	-	-	-	IA	4'-0"	-	102A
102B	CLERK	2A	1A	2A	-	-	-	IA	4'-0"	-	102B
103	OFFICE	2A	1A	2A	2A	2A	2A	IA	4'-0"	-	103
104	OFFICE	2A	1A	2A	2A	2A	2A	IA	4'-0"	-	104
105	STUDENT LOBBY	10A	6A	-	-	-	-	IA	4'-0"	-	105
106	NURSE	3A	1A	2A	2A	2A	2A	IA	4'-0"	-	106
107	VESTIBULE	2A	1A	2A	2A	2A	2A	IA	4'-0"	-	107
108	TOILET (UNSEX)	8A	5A	4A	4A	4A	4A	2B	4'-0"	-	108
109	TOILET (UNSEX)	8A	5A	4A	4A	4A	4A	2B	4'-0"	-	109
110	TOILET (UNSEX)	8A	5A	4A	4A	4A	4A	2B	4'-0"	-	110
111	CONFERENCE	2A	1A	1A	1A	1A	1A	IA	4'-0"	-	111
112	BOOK STORAGE	2A	1A	1A	1A	1A	1A	IA	4'-0"	-	112
113	IMC	1A2A	1A	1A	1A	1A	1A	IA15B	VARIABLES	-	113
114	VESTIBULE	2A	1A	2A	2A	2A	2A	IA	4'-0"	-	114
201	MULTI-PURPOSE	1A	1A	2A5B/A1A	2A5B/A1A	2A15B	2A5B/A1A	5A	4'-0"	-	201
202	STAGE	5E	1A	5B	2A15B	-	2A15B	3C	11'-0"	-	202
203	STORAGE	5C	4C	5C	5C	5C	5C	3C	11'-0"	-	203
204	DRESS ROOM	5E	1A	5B	5B	5B	5B	3C	11'-0"	-	204
205	HCLIFT	1A	1A	5B	5B	5B	5B	3C	11'-0"	-	205
206	FAN ROOM	5C	4C	5C	5C	5C	5C	3C	11'-0"	-	206
207	MEN	8A	5A	5B14A	5B14A	5B14A	5B14A	3B	4'-0"	-	207
208	WOMEN	8A	5A	5B14A	5B14A	5B14A	5B14A	3B	4'-0"	-	208
209	CUSTOMER	5C	4C	5C	5C	5C	5C	3C	11'-0"	-	209
210	HEATER	5C	4C	5C	5C	5C	5C	3C	11'-0"	-	210
211	SOLID DISH	5C	4C	5B15C	5B15C	5B15C	5B15C	3C	11'-0"	-	211
212	CORRIDOR	3A	1A	5B15C/1B	5B15C/1B	5B15C	5B15C/1B	3C	4'-0"	-	212
213	CORRIDOR	3A	1A	5B15C/1B	5B15C/1B	5B15C	5B15C/1B	3C	4'-0"	-	213
214	KITCHEN	3A	1A	1B15B	1B15B	1B15B	1B15B	3C	4'-0"	-	214
215	FAULTY DINNER	1A	1A	1B15B	1B15B	1B15B	1B15B	3C	4'-0"	-	215
216	STORAGE	3A	1A	5B	5B	5B	5B	3B	4'-0"	-	216
217	DRY STORAGE	3A	1A	5B	5B	5B	5B	3B	4'-0"	-	217
218	CHEF OFFICE	2A	1A	2A	2A	2A	2A	2B	4'-0"	-	218
219	TOILET (UNSEX)	8A	5A	5B/4A	5B/4A	5B/4A	5B/4A	2B	4'-0"	-	219
220	LOCKERS	3A	1A	1B	1B	1B	1B	2B	4'-0"	-	220
221	WALK IN	3A	1A	1A	1A	1A	1A	2A	4'-0"	-	221
222	CAN WASH	5C	4C	5C	5C	5C	5C	3C	11'-0"	-	222
223	FAN ROOM	5C	4C	5C	5C	5C	5C	3C	11'-0"	-	223
301	KINDERGARTEN	1A2A	1A	2A	2A	2A	2A	1A	4'-0"	-	301
302	TOILET (UNSEX)	8A	5A	4A/5B	4A/5B	4A15B	4A15B	2B	4'-0"	-	302
303	VESTIBULE	1A	1A	1B	1B	1B14A	1B14A	1A	4'-0"	-	303
304	WORK ROOM	2A	1A	2A	2A	2A	2A	1A	4'-0"	-	304
305	TOILET (UNSEX)	8A	5A	4A/5B	4A/5B	4A15B	4A15B	2B	4'-0"	-	305
306	VESTIBULE	1A	1A	1B	1B	1B14A	1B14A	1A	4'-0"	-	306
307	KINDERGARTEN	1A2A	1A	2A	2A	2A	2A	1A	4'-0"	-	307
308	TOY STORAGE	5C	4C	5C	5C	5C	5C	3C	11'-0"	-	308
401	BOYS	8A	5A	4A15B	4A15B	4A15B	4A15B	2B	4'-0"	-	401
402	GIRLS	8A	5A	4A15B	4A15B	4A15B	4A15B	2B	4'-0"	-	402
403	TRANS VAULT	5C	4C	5C	5C	5C	5C	3C	11'-0"	-	403
404	CUSTOMER	5C	4C	5C	5C	5C	5C	3C	11'-0"	-	404
405	LAUNDRY	5C	4C	5C	5C	5C	5C	3C	11'-0"	-	405
406	CLASSROOM	1A	1A	2A	2A	2A	2A	1A	4'-0"	-	406
407	CLASSROOM	1A	1A	2A	2A	2A	2A	1A	4'-0"	-	407
408	CLASSROOM	1A	1A	2A	2A	2A	2A	1A	4'-0"	-	408
409	CLASSROOM	1A	1A	2A	2A	2A	2A	1A	4'-0"	-	409
410	CLASSROOM	1A	1A	2A	2A	2A	2A	1A	4'-0"	-	410
501	BOYS	8A	5A	4A15B	4A15B	4A15B	4A15B	2B	4'-0"	-	501
502	GIRLS	8A	5A	4A15B	4A15B	4A15B	4A15B	2B	4'-0"	-	502
503	WOMEN	8A	5A	4A/5B	4A/5B	4A/5B	4A/5B	2B	4'-0"	-	503
504	MEN	8A	5A	4A/5B	4A/5B	4A15B	4A15B	2B	4'-0"	-	504
505	TEACHERS LOUNGE	3A12A	1A	1B/5B	1B/5B	1B15B	1B15B	1A	4'-0"	-	505
506	LIBRARY	1A2A	1A	2A	2A	2A	2A	1A	4'-0"	-	506
507	CLASSROOM	1A	1A	2A	2A	2A	2A	1A	4'-0"	-	507
508	CLASSROOM	1A	1A	2A	2A	2A	2A	1A	4'-0"	-	508
509	CLASSROOM	1A	1A	2A	2A	2A	2A	1A	4'-0"	-	509
510	CLASSROOM	1A	1A	2A	2A	2A	2A	1A	4'-0"	-	510
601	BOYS	8A	5A	4A15B	4A15B	4A15B	4A15B	2B	4'-0"	-	601
602	GIRLS	8A	5A	4A15B	4A15B	4A15B	4A15B	2B	4'-0"	-	602
603	CONSLOR	2A	1A	2A	2A	2A	2A	1A	4'-0"	-	603
604	ATHLETIC STORAGE	5C	4C	5C	5C	5C	5C	3C	11'-0"	-	604
605	WORKROOM	5C	4C	5B	5B	5B	5B	3B	4'-0"	-	605
606	CLASSROOM	1A	1A	2A	2A	2A	2A	1A	4'-0"	-	606
607	CLASSROOM	1A	1A	2A	2A	2A	2A	1A	4'-0"	-	607
608	CLASSROOM	1A	1A	2A	2A	2A	2A	1A	4'-0"	-	608
609	CLASSROOM	1A	1A	2A	2A	2A	2A	1A	4'-0"	-	609
610	CLASSROOM	1A	1A	2A	2A	2A	2A	1A	4'-0"	-	610

FLOORS

1. VINYL COMPOSITION TILE (2X12)
2. CARPET
3. SHEET VINYL
4. RUBBER
5. EXISTING
6. CONCRETE
7. ACCENT CARPET
8. UNGLAZED CERAMIC MOSAIC TILE W/SETTING BED
9. 1/4" COX FLOOR UNDERLAMENT
10. GRANITE TILE W/SETTING BED

BASE

1. 4" RUBBER TORSSET
2. COVER SHEET VINYL - SEE DET. (A01)
3. RUBBER TORSET STRINGER
4. EXISTING
5. 6" COVER GLAZED CERAMIC TILE
6. GRANITE TILE

WALLS

1. 1/2" VENEER PLASTER FINISH - SEE DET. (20)
2. VINYL COVERED TACKABLE WALLBOARD WITH 5/8" GYP BOARD TYPE 'X'
3. VINYL WALL COVERING WITH 5/8" GYP BOARD TYPE 'X'
4. GLAZED CERAMIC TILE W/SETTING BED - SEE SPEC.
5. EXISTING
6. FRP

CEILING

1. SUSPENDED 2'-0" X 4'-0" T-BAR CEILING SYSTEM W/ LAY-ON ACOUSTIC TILE PANELS.
2. 5/8" TYPE 'X' GYP BD W/ 1/2" VENEER (A01)
3. PLASTER FINISH - SEE DET.
4. EXISTING
5. 5/8" TYPE 'X' GYP BD - TAPE AND FINISH
6. 1/2" TYPE 'X' GYP BOARD - TAPE & FINISH
7. 1/2" TYPE 'X' GYP BOARD - TAPE & FINISH AS INDICATED
8. STAINLESS STEEL

FINISH SCHED. NOTES

1. PATCH BACK AND FINISH ALL (E) FINISHES DISBURBED BY ADDITION NEW WALL FINISHES AT INSETS SHALL BE FLUSH W/ (E) ADJACENT WALLS. SEE INTERIOR ELEVATIONS FOR FINISHES TO BE REMOVED OR RELOCATING WALLS. FINISHES OR BLOCKING INSTALLATION TO MATCH FINISHES AND FINISHES INDICATED ON ROOM FINISH SCHEDULE SHALL BE IN ACCORDANCE WITH THE CONSOLE OF AMERICA INSTALLATION PROCEDURES (CURRENT EDITION).
3. SEE INTERIOR ELEVATIONS FOR SOFFIT HEIGHTS
4. SEE REFLECTED CEILING PLAN FOR VOLUME HEIGHTS
5. ALL WOOD TRIMS AT DOORS AND WINDOWS SHALL BE PAINTED IN SEMI-GLOSS ENAMEL.

FINISHERS

- A. FACTORY FINISH
- B. PAINT - PER SPECS
- C. EXISTING
- D. SEALER
- E. SAND & CLEARCOAT



FINISH SCHEDULE

FINISH SCHEDULE

FINISH SCHEDULE

FINISH SCHEDULE

FINISH SCHEDULE

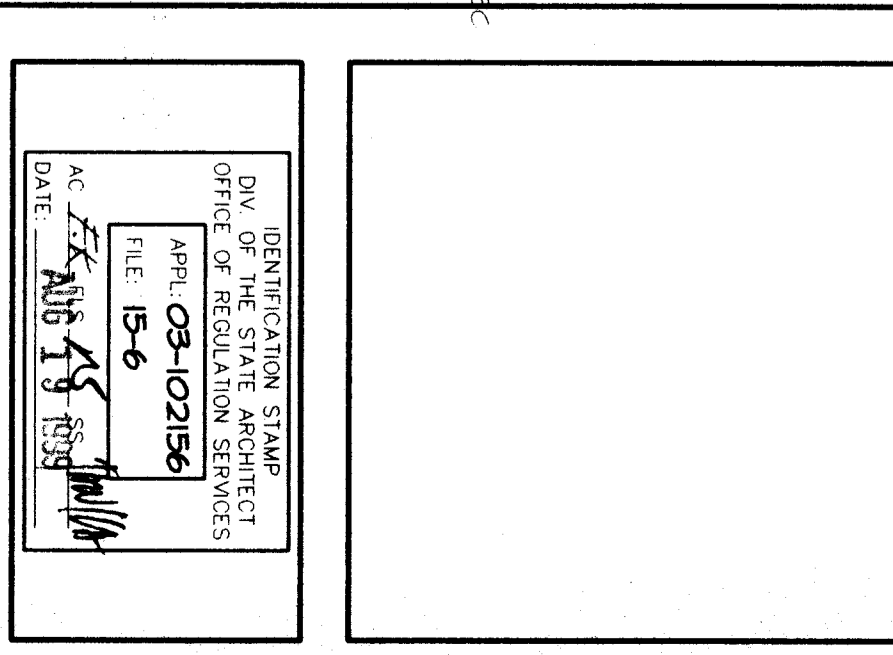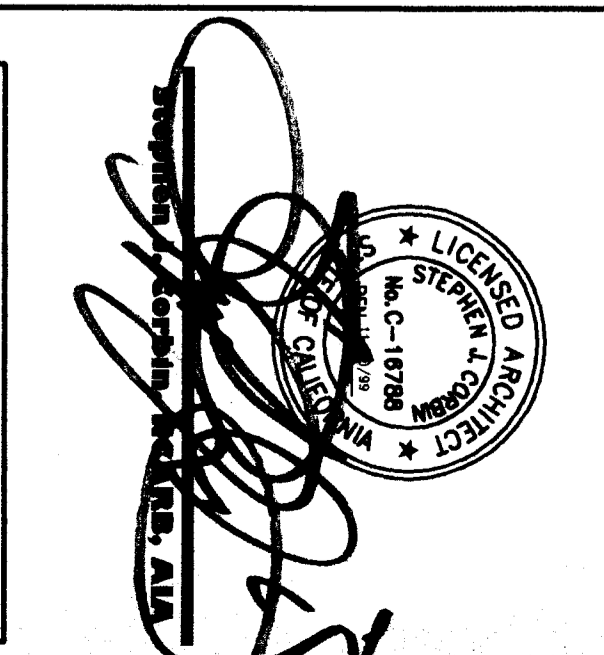

RUTH HARDING SCHOOL
MODERNIZATION
 3201 PICO AVE.
 FOR
BAKERSFIELD CITY SCHOOL DISTRICT
 BAKERSFIELD, KERN COUNTY, CALIFORNIA

FINISH SCHEDULE

DATE: 12/15/96

BY: [Signature]

FOR: [Signature]

PROJECT: RUTH HARDING SCHOOL MODERNIZATION

DATE: 12/15/96

BY: [Signature]

FOR: [Signature]

PROJECT: RUTH HARDING SCHOOL MODERNIZATION

MARK DATE REVISIONS

VOID
