

**CHANGE ORDER FORM**

Bakersfield City School District  
1501 Feliz Drive  
Bakersfield, CA 93307

**CHANGE ORDER NO.:**

HMES-01-005

**CHANGE ORDER**

**Project / Bid No. / DSA No.:** Horace Mann ES – Campus HVAC  
System Upgrade / 22214.00-32-HVAC / DSA # 03-122640

**Date:** 9/29/2025  
**DSA File No.:** 15-6  
**DSA Appl. No.:** 03-122640

The following parties agree to the terms of this Change Order:

**Owner: Bakersfield City School District**  
**1300 Baker St.**  
**Bakersfield, CA, 93305**

**Contractor: HMES- 01 – PARC Environmental**  
**2864 E Dorothy Ave.**  
**Fresno, CA, 93706**

**Architect: AP Architects**  
**3434 Truxtun Ave., Suite 240**  
**Bakersfield, CA, 93301**

Reference	Description	Cost	Days Ext.
PCO #05 Requested by: Performed by: Reason:	Lead Remediation at Steel – Building B and C Unforeseen Existing Conditions Abatement Prime Contractor Primer at steel trusses contains lead. Lead primer was required to be abated in order to weld new steel connections.	\$25,075.49	
PCO # Requested by: Performed by: Reason:			
PCO # Requested by: Performed by: Reason:			
Contract time will be adjusted as follows:		Original Contract Amount:	\$989,000.00
Previous Completion Date: <u>5/11/2026</u>		Amount of Previously Approved Change Order(s):	\$1,231.92
<u>0</u> Calendar Days Extension (zero unless otherwise indicated)		Amount of this Change Order:	\$25,075.49
Current Completion Date: <u>5/11/2026</u>		Contract Amount:	\$1,015,307.41

The undersigned Contractor approves the foregoing as to the changes, if any, to the Contract Price specified for each item, and as to the extension of time allowed, if any, for

**BAKERSFIELD CITY SCHOOL DISTRICT**

**CHANGE ORDER FORM**  
**DOCUMENT 00 63 63-1**



completion of the entire work as stated therein, and agrees to furnish all labor, materials and services and perform all work necessary to complete any additional work specified for the consideration stated therein. Submission of sums which have no basis in fact or which Contractor knows are false are at the sole risk of Contractor and may be a violation of the False Claims Act set forth under Government Code section 12650 et seq.

This change order is subject to approval by the governing board of this District and must be signed by the District. Until such time as this change order is approved by the District's governing board and executed by a duly authorized District representative, this change order is not effective and not binding.

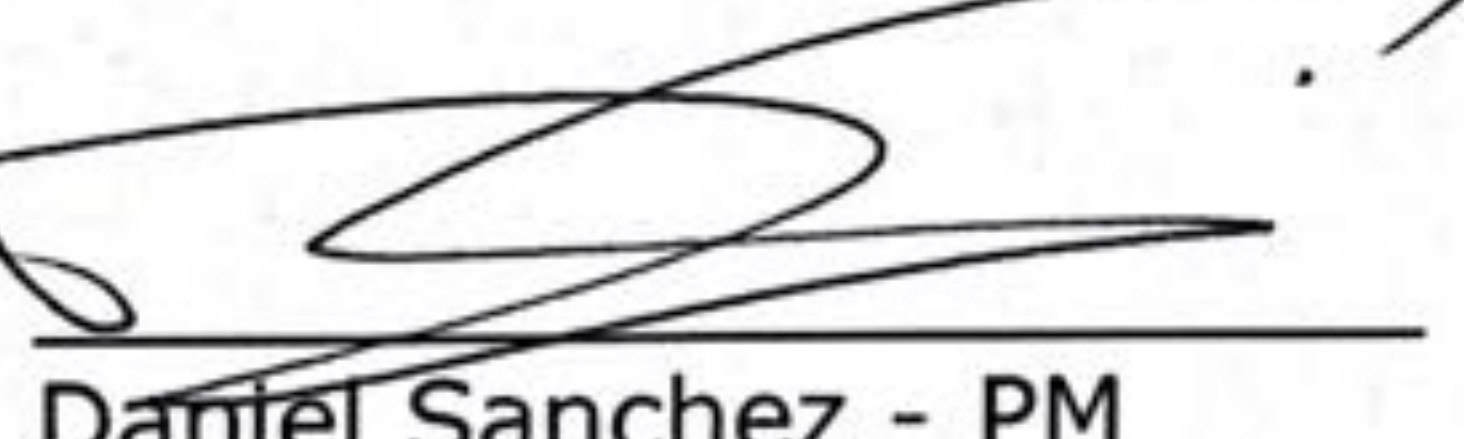
It is expressly understood that the compensation and time, if any, granted herein represent a full accord and satisfaction for any and all time and cost impacts of the items herein, and Contractor waives any and all further compensation or time extension based on the items herein. The value of the extra work or changes expressly includes any and all of the Contractor's costs and expenses, and its subcontractors, both direct and indirect, resulting from additional time required on the project or resulting from delay to the project including without limitation, cumulative impacts. Any costs, expenses, damages or time extensions not included are deemed waived.

**Signatures:**


District: Assistant Superintendent, Business Services

Contractor: PARC Environmental

  
Sherry Gladin Date 11/4/25

  
Daniel Sanchez - PM Date 11/03/2025

Architect: AP Architect

  
J. Patrick Fogarty Date 11/4/25

END OF DOCUMENT
