

REQUEST FOR QUOTATION

(Revised June 2019)

Date: 04/08/2024 **M&O Employee Requesting Quote:** Leonard Zasoski, Jr.

Project Name: Evergreen Elementary Asphalt Slurry & Restriping

Quote Due Date: April 12, 2024 2:00pm **Quote is valid until:** _____

Pursuant to Labor Code § 1720 et. seq., this work is considered a “Public Work” and is subject to the payment of prevailing wages if the total project cost is over \$1,000. Proof of a valid Contractor/Specialty License, DIR Registration, Worker’s Compensation, and liability insurance is required before work can begin.

If awarded, you will be required to enter certified payroll reports (electronically) into the Department of Industrial Relations (DIR) eCPR website located at: <https://apps.dir.ca.gov/ecpr/DAS/AltLogin>

Quantity	Description/Scope of Work to be Performed	Unit Price	Extended Price
Lump	1. Provide a base bid for the asphalt slurry and restriping. 2. Provide an alternate bid for filling cracks and patching potholes. Project will be awarded on the base bid only. <ul style="list-style-type: none"> • Attachment “A” showing the area for the Asphalt Slurry • Attachment “B” project schedule. • Attachment “C” scope of work. 		
(Attach additional sheets if necessary) BASE BID			
(Attach additional sheets if necessary) ALTERNATE #1			

If the District accepts this Quotation for services to be rendered to the District under the amount of \$60,000, I agree with the terms and conditions of the Bakersfield City School District’s Field Contract for Services. (A sample contract will be provided upon request.)

If applicable, initial to acknowledge receipt of addenda(s): #1 _____, #2 _____, #3 _____, and #4 _____.

I certify that I have inspected the work site; have met with the District representative; and fully understand the entire scope of work to be performed. I also confirm that I possess all of the proper licenses and certifications that are necessary to complete this work.

Please type or print legibly

Company Name: _____

Address: _____

Contractor’s License No.: _____ DIR Registration No.: _____ Tax ID: _____

Contact Person: _____ Phone No: _____ Fax No.: _____

E-mail address (Must include): _____

Signature of Authorized Person: _____ Date: _____

REQUEST FOR QUOTATION (cont.)

(Revised January 2019)

**DIR Classification(s) of workers to be utilized.
Check all that apply.**

<input type="checkbox"/> Asbestos <input type="checkbox"/> Cement Masons <input type="checkbox"/> Elevator Mechanic <input type="checkbox"/> Landscape Maint. <input type="checkbox"/> Pipe Trades/Plumber <input type="checkbox"/> Sound/Communications <input type="checkbox"/> Tile Workers	<input type="checkbox"/> Bricklayers <input type="checkbox"/> Drywall Finisher <input type="checkbox"/> Glazier <input type="checkbox"/> Operating Engineer <input type="checkbox"/> Plaster <input type="checkbox"/> Surveyors	<input type="checkbox"/> Carpenters <input type="checkbox"/> Drywall Lather <input type="checkbox"/> Iron Worker <input type="checkbox"/> Modular Furn. Installer <input type="checkbox"/> Roofers <input type="checkbox"/> Teamster	<input type="checkbox"/> Carpet/Linoleum <input type="checkbox"/> Electrician <input type="checkbox"/> Laborer <input type="checkbox"/> Painter <input type="checkbox"/> Sheet metal/HVAC <input type="checkbox"/> Telecom Technician
--	--	---	--

Classifications and wage rates can be found at: <http://www.dir.ca.gov/oprl/PWD/index.htm>

DIR Prevailing Wage Hot Line: (415) 703-4774

Important Notice: California new law (SB 854) provides that, "A contractor or subcontractor shall not be qualified to bid on, be listed in a bid proposal, subject to the requirements of Section 4104 of the Public Contract Code, or engage in the performance of any contract for public work, as defined in this chapter, unless currently registered and qualified to perform public work pursuant to Labor Code Section 1725.5." Please go to <http://www.dir.ca.gov/Public-Works/PublicWorks.html> for more information and to register. This project is subject to monitoring by the Department of Industrial Relations.

BCSD Office Use:

Accepted by Bakersfield City School District:

Print Name and Title: Leonard Zasoski, Jr. – Assistant Director II, Maintenance, Operations & Facilities


Signature: _____ Date: _____

Budget Code: _____ PO/Contract No.: _____

Est. Project Start Date: _____ Est. Project End Date: _____

PWC-100 Processing Date: _____

PWC-100 Data Entry Website: <https://www.dir.ca.gov/pwc100ext/>

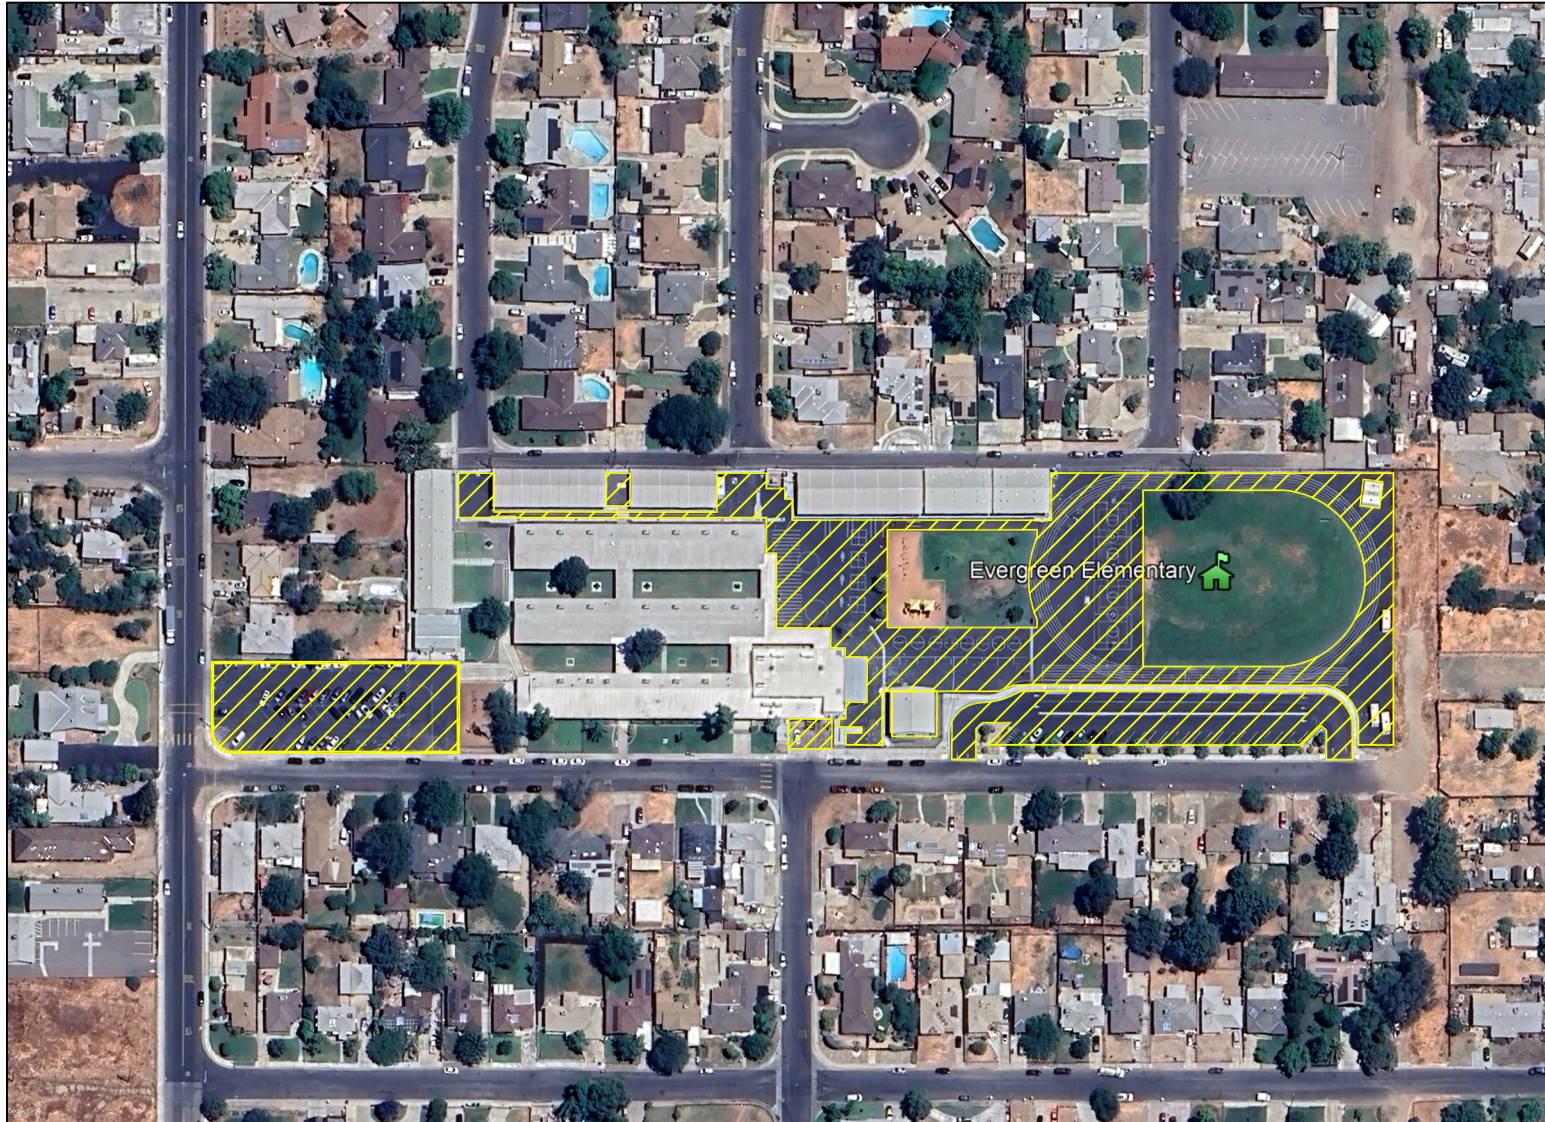

Asphalt Area: $\pm 135,805$ sq. ft.

EVERGREEN ELEMENTARY SCHOOL

ASPHALT SLURRY

3-13-24



Activity ID	Act. Assignment	Activity Name	Original Duration	Start	Finish	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J
2024 Deferred Projects						14-Aug-24, 2024: Deferred Projects																																				
Asphalt Projects						150 15-Jan-24 14-Aug-24																																				
Asphalt Slurry Projects						104 11-Mar-24 01-Aug-24																																				
Pre-Construction Activities						65 11-Mar-24 10-Jun-24																																				
ASPC-1000	BCSD	Create Bid Scope / RFQ	20	11-Mar-24*	05-Apr-24	Create Bid Scope / RFQ																																				
ASPC-1010	BCSD	Project Quotes	1	08-Apr-24	08-Apr-24	Project Quotes																																				
ASPC-1020	Contractors	Bid Projects	5	08-Apr-24	12-Apr-24	Bid Projects																																				
ASPC-1040	Contractors	Bids Due	1	15-Apr-24	15-Apr-24	Bids Due																																				
ASPC-1050	BCSD	Review Bids	1	16-Apr-24	16-Apr-24	Review Bids																																				
ASPC-1060	General	Notice to Awards	1	17-Apr-24	17-Apr-24	Notice to Awards																																				
ASPC-1070	BCSD	Contracts & Insurance	10	18-Apr-24	01-May-24	Contracts & Insurance																																				
ASPC-1080	BCSD	Notice to Proceed	1	02-May-24	02-May-24	Notice to Proceed																																				
Submittals						37 18-Apr-24 10-Jun-24																																				
Slurry Product						37 18-Apr-24 10-Jun-24																																				
SLU-1000	Contractors	Slurry Product (Contractor Prepare Submittal)	5	18-Apr-24	24-Apr-24	Slurry Product (Contractor Prepare Submittal)																																				
SLU-1010	BCSD	Slurry Product (BCSD Review Submittal)	1	25-Apr-24	25-Apr-24	Slurry Product (BCSD Review Submittal)																																				
SLU-1020	Contractors	Slurry Product (Procurement)	2	06-Jun-24	10-Jun-24	Slurry Product (Procurement)																																				
Asphalt Slurry Construction						44 03-Jun-24 01-Aug-24																																				
Asphalt Slurry Projects Complete by June 30th						23 03-Jun-24 03-Jul-24																																				
Curran						17 03-Jun-24 25-Jun-24																																				
C-1000	General	Start Construction	0	03-Jun-24*		Start Construction																																				
C-1010	BP 01 Asphalt Slurry	Clean Paving Areas	3	03-Jun-24	05-Jun-24	Clean Paving Areas																																				
C-1001	BP 01 Asphalt Slurry	Alternate 1 Patch Pot Holes & Cracks over 1/2" Wide	3	06-Jun-24	10-Jun-24	Alternate 1 Patch Pot Holes & Cracks over 1/2" Wide																																				
C-1020	BP 01 Asphalt Slurry	Apply Slurry Coat	5	10-Jun-24	17-Jun-24	Apply Slurry Coat																																				
C-1030	BP 01 Asphalt Slurry	Slurry Cure Time	3	17-Jun-24	20-Jun-24	Slurry Cure Time																																				
C-1040	BP 01 Asphalt Slurry	Stripe Playfield & Parking Area	3	20-Jun-24	25-Jun-24	Stripe Playfield & Parking Area																																				
C-1050	General	Project Complete	0		25-Jun-24	Project Complete																																				
Hort						17 06-Jun-24 28-Jun-24																																				
H-1000	General	Start Construction	0	06-Jun-24		Start Construction																																				
H-1010	BP 01 Asphalt Slurry	Clean Paving Areas	3	06-Jun-24	10-Jun-24	Clean Paving Areas																																				
H-1120	BP 01 Asphalt Slurry	Alternate 1 Patch Pot Holes & Cracks over 1/2" Wide	3	11-Jun-24	13-Jun-24	Alternate 1 Patch Pot Holes & Cracks over 1/2" Wide																																				
H-1020	BP 01 Asphalt Slurry	Apply Slurry Coat	5	13-Jun-24	20-Jun-24	Apply Slurry Coat																																				
H-1030	BP 01 Asphalt Slurry	Slurry Cure Time	3	20-Jun-24	25-Jun-24	Slurry Cure Time																																				
H-1040	BP 01 Asphalt Slurry	Stripe Playfield & Parking Area	3	25-Jun-24	28-Jun-24	Stripe Playfield & Parking Area																																				
H-1050	General	Project Complete	0		28-Jun-24	Project Complete																																				
Evergreen						17 11-Jun-24 03-Jul-24																																				
E-1000	General	Start Construction	0	11-Jun-24		Start Construction																																				
E-1010	BP 01 Asphalt Slurry	Clean Paving Areas	3	11-Jun-24	13-Jun-24	Clean Paving Areas																																				
E-1060	BP 01 Asphalt Slurry	Alternate 1 Patch Pot Holes & Cracks over 1/2" Wide	3	14-Jun-24	18-Jun-24	Alternate 1 Patch Pot Holes & Cracks over 1/2" Wide																																				
E-1020	BP 01 Asphalt Slurry	Apply Slurry Coat	5	18-Jun-24	25-Jun-24	Apply Slurry Coat																																				
E-1030	BP 01 Asphalt Slurry	Slurry Cure Time	3	25-Jun-24	28-Jun-24	Slurry Cure Time																																				
E-1040	BP 01 Asphalt Slurry	Stripe Playfield & Parking Area	3	28-Jun-24	03-Jul-24	Stripe Playfield & Parking Area																																				
E-1050	General	Project Complete	0		03-Jul-24	Project Complete																																				

█ Actual Work
 █ Critical Remaining Work
 Summary
█ Remaining Work
 ◆ Milestone

Date	Revision	Checked	Approved
12-Mar-24	Asphalt Slurry Projects Baseline-Bid (Attachment B)		

**Bakersfield City School District
Deferred Projects Summer 2024**



Bakersfield City School District

Activity ID	Act. Assignment	Activity Name	Original Duration	Start	Finish	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J
Asphalt Slurry Projects Starting After July 1st			24	01-Jul-24	01-Aug-24	▼ 01-Aug-24, Asphalt Slurry Projects Starting After July 1st																																				
Garza			17	01-Jul-24	23-Jul-24	▼ 23-Jul-24, Garza																																				
G-1000	General	Start Construction	0	01-Jul-24*		◆ Start Construction																																				
G-1010	BP 01 Asphalt Slurry	Clean Paving Areas	3	01-Jul-24	03-Jul-24	▮ Clean Paving Areas																																				
G-1060	BP 01 Asphalt Slurry	Alternate 1 Patch Pot Holes & Cracks over 1/2" Wide	3	04-Jul-24	08-Jul-24	▮ Alternate 1 Patch Pot Holes & Cracks over 1/2" Wide																																				
G-1020	BP 01 Asphalt Slurry	Apply Slurry Coat	5	08-Jul-24	15-Jul-24	▮ Apply Slurry Coat																																				
G-1030	BP 01 Asphalt Slurry	Slurry Cure Time	3	15-Jul-24	18-Jul-24	▮ Slurry Cure Time																																				
G-1040	BP 01 Asphalt Slurry	Stripe Playfield & Parking Area	3	18-Jul-24	23-Jul-24	▮ Stripe Playfield & Parking Area																																				
G-1050	General	Project Complete	0		23-Jul-24	◆ Project Complete																																				
Harris			17	05-Jul-24	29-Jul-24	▼ 29-Jul-24, Harris																																				
H-1060	General	Start Construction	0	05-Jul-24		◆ Start Construction																																				
H-1070	BP 01 Asphalt Slurry	Clean Paving Areas	3	05-Jul-24	09-Jul-24	▮ Clean Paving Areas																																				
H-1130	BP 01 Asphalt Slurry	Alternate 1 Patch Pot Holes & Cracks over 1/2" Wide	3	10-Jul-24	12-Jul-24	▮ Alternate 1 Patch Pot Holes & Cracks over 1/2" Wide																																				
H-1080	BP 01 Asphalt Slurry	Apply Slurry Coat	5	12-Jul-24	19-Jul-24	▮ Apply Slurry Coat																																				
H-1090	BP 01 Asphalt Slurry	Slurry Cure Time	3	19-Jul-24	24-Jul-24	▮ Slurry Cure Time																																				
H-1100	BP 01 Asphalt Slurry	Stripe Playfield & Parking Area	3	24-Jul-24	29-Jul-24	▮ Stripe Playfield & Parking Area																																				
H-1110	General	Project Complete	0		29-Jul-24	◆ Project Complete																																				
Jefferson			17	10-Jul-24	01-Aug-24	▼ 01-Aug-24, Jefferson																																				
J-1000	General	Start Construction	0	10-Jul-24		◆ Start Construction																																				
J-1010	BP 01 Asphalt Slurry	Clean Paving Areas	3	10-Jul-24	12-Jul-24	▮ Clean Paving Areas																																				
J-1060	BP 01 Asphalt Slurry	Alternate 1 Patch Pot Holes & Cracks over 1/2" Wide	3	15-Jul-24	17-Jul-24	▮ Alternate 1 Patch Pot Holes & Cracks over 1/2" Wide																																				
J-1020	BP 01 Asphalt Slurry	Apply Slurry Coat	5	17-Jul-24	24-Jul-24	▮ Apply Slurry Coat																																				
J-1030	BP 01 Asphalt Slurry	Slurry Cure Time	3	24-Jul-24	29-Jul-24	▮ Slurry Cure Time																																				
J-1040	BP 01 Asphalt Slurry	Stripe Playfield & Parking Area	3	29-Jul-24	01-Aug-24	▮ Stripe Playfield & Parking Area																																				
J-1050	General	Project Complete	0		01-Aug-24	◆ Project Complete																																				
Washington Middle School			150	15-Jan-24	14-Aug-24	▮ Washington Middle School																																				
McKinley Projects			152	15-Jan-24	14-Aug-24	▮ McKinley Projects																																				
Cato - Sport Court Restripe			89	01-Apr-24	05-Aug-24	▮ Cato - Sport Court Restripe																																				
Emerson Projects			69	18-Mar-24	21-Jun-24	▮ Emerson Projects																																				
Fall Material @ Elementary Playgrounds			104	19-Feb-24	15-Jul-24	▮ Fall Material @ Elementary Playgrounds																																				
Fall Mats @ Elementary Playgrounds			94	04-Mar-24	15-Jul-24	▮ Fall Mats @ Elementary Playgrounds																																				
Site Sweeping			82	15-Apr-24	08-Aug-24	▮ Site Sweeping																																				

█ Actual Work
 █ Critical Remaining Work
 ▼ Summary
█ Remaining Work
 ◆ Milestone

Date	Revision	Checked	Approved
12-Mar-24	Asphalt Slurry Projects Baseline-Bid (Attachment B)		

Evergreen - Asphalt Slurry 2024

Scope of Work

General Items:

- Summer working hours shall be 6:00 a.m. to 2:30 p.m. or on an agreed upon time between the contractor and the district.
- **Construction schedule provided by BCSD. See Attachment "B"**
- Apply two coats of slurry with slurry buggy over at each site.
- Thoroughly clean the asphalt prior to the slurry application.
- Slurry material not to be greater than 25%.
- No line bleed through from existing striping.
- Contractor will redo all striping covered by the slurry to match existing layouts after the asphalt slurry work.
- Prior to asphalt slurry placement, contractor to field verify and confirm layout of all markings on the pavement by field measurements and pictures.
- See **Attachment "A"** for area to receive the slurry coat. **Note: Contractor shall be responsible for all quantities and measurements.**

Alternate:

- Provide an alternate bid to patch asphalt cracks ½" and larger, potholes prior to the slurry application. **Note: Project will be awarded on the base bid only.**
- If you would like to visit the site, please contact Brenda Orozco at (661)631-5883 to schedule the site visit.

Protection:

- The Contractor shall always take all precautions to avoid damaging structures around the work area. The Contractor shall be responsible for, and liable for, all damage or ill effects caused by a lack of adequate protection against the hazards associated with their work. The Contractor shall carry adequate insurance and he shall protect the district from all liens or damages arising from or caused by his work.

Disposal:

- The Contractor shall thoroughly clean the area as work progresses. After completion of work, the Contractor shall remove all debris resulting from this work and shall remove all splatters or spills from other surfaces adjacent to the work. The buildings and the site premises shall be left in a condition that is acceptable to the district.
